ID	Description	Original Duration	Start	Finish	Predecessors	Successors
Timpview High School Phase 2 Remodel						
Milestones						
10	Project Duration	871	05/12/21A	09/11/24	240FS*, 5760F	
30	Phase 2A Duration	588	06/29/21A	09/28/23	40SS*, 120FF	
22	South East Athletics Wing Area 02A	293	09/28/21A	11/10/22	3980SS*, 417	
20	Substantial Completion	0		09/11/24	5760FF*	
Phase 2A						
50	Masonry Complete	0		10/21/22	2480FF, 3170	
25	South East Athletics Wing Turnover - Area 02A	0		11/10/22	417FF*	
60	Concrete Complete	0		12/16/22	2190FF*, 268	
70	Building Dry-In	0		12/30/22	3060FF*	
90	Framing Complete	0		01/20/23	2900FF*	
100	MEP Rough-In Complete	0		02/10/23	2910FF*	
80	Exterior Finishes Complete	0		05/16/23	3830FF*	
110	Interior Finishes Complete	0		06/26/23	3040FF*	
120	Phase 2A Complete	0		09/28/23	3950FF*	30FF
Phase 2B						
130	Phase 2B Duration	249	09/29/23	09/11/24	140SS*, 220F	
140	Construction Start	0	09/29/23		4880SS*	130SS*
150	Masonry Complete	0		02/01/24	5290FF*	
160	Concrete Complete	0		03/07/24	5480FF*	
170	Building Dry-In	0		04/01/24	5670FF*	
180	Framing Complete	0		04/11/24	5510FF*	
190	MEP Rough-In Complete	0		04/18/24	5520FF*	
200	Exterior Finishes Complete	0		05/27/24	5720FF*	
210	Interior Finishes Complete	0		08/16/24	5650FF*	
220	Phase 2B Complete	0		09/11/24	5760FF*	130FF
Construction						
Phase 2A - North Academic Wing						
Area 12						
Level 1						
1090	1st Side Drywall	5	12/12/22	12/16/22	1650FS*, 108	1110FS*, 128
1100	Insulation	3	12/14/22	12/16/22	1090FS-3d*	1110FS*
1110	2nd Side Drywall	5	12/19/22	12/23/22	1090FS*, 110	1120FS*, 469
1120	Tape & Finish Walls	8	12/26/22	01/04/23	1110FS*	1130FS*
1130	Paint	5	01/05/23	01/11/23	1120FS*	1140FS-3d*
1140	ACT Grid	5	01/09/23	01/13/23	1130FS-3d*	1150FS*, 117
1150	MEP Ceiling Finishes	10	01/16/23	01/27/23	1140FS*	1180FS-5d*
1160	Interior Glazing	5	01/16/23	01/20/23	1140FS*	
1170	Millwork	10	01/16/23	01/27/23	1140FS*	1190FS*
1180	MEP Wall Finishes	10	01/23/23	02/03/23	1150FS-5d*	1200FS*, 121
1190	Countertops	5	01/30/23	02/03/23	1170FS*	1200FS*
1200	Flooring	15	02/06/23	02/24/23	1180FS*, 119	3920FS, 393
1210	Doors & Hardware	5	04/07/23	04/13/23	1180FS, 1200	1970FS

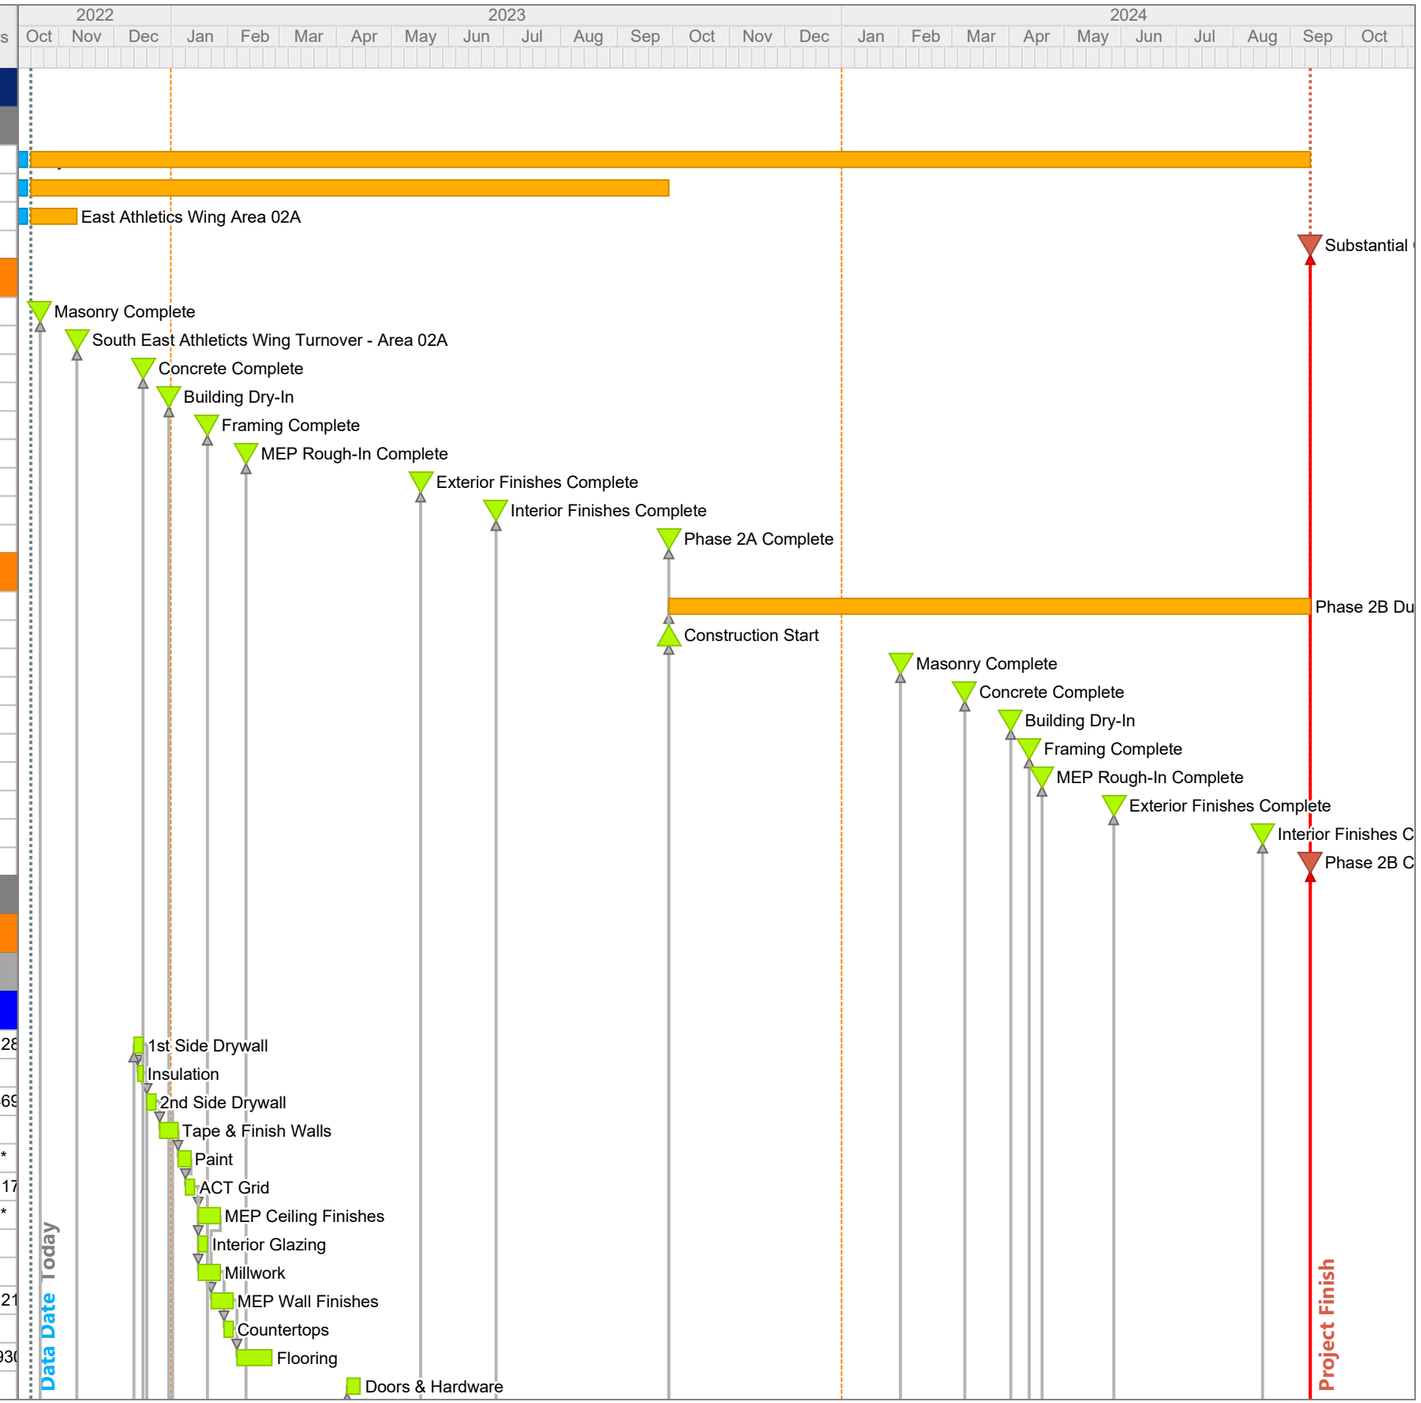

Start Date: 05/01/21
Finish Date: 09/11/24
Data Date: 10/17/22
Run Date: 10/17/22

Page 1A

Timpview High School Rebuild

WESTLAND

ID	Description	Original Duration	Start	Finish	Predecessors	Successors
Level 2						
1265	Kitchen Fume Hoods	15	10/10/22A	10/28/22	1260FS*	1280FS
1280	1st Side Drywall	5	12/19/22	12/23/22	1090FS*, 127(	1300FS, 129(
1290	Insulation	3	12/26/22	12/28/22	1280FS*	1300FS*
1300	2nd Side Drywall	5	12/29/22	01/04/23	1280FS, 1290	1310FS*
1310	Tape & Finish Walls	8	01/05/23	01/16/23	1300FS*	1320FS*
1320	Paint	5	01/17/23	01/23/23	1310FS*	1330FS*
1330	ACT Grid	5	01/24/23	01/30/23	1320FS*	1340FS*, 136
1340	MEP Ceiling Finishes	10	01/31/23	02/13/23	1330FS*	1370FS-5d*
1350	Interior Glazing	5	01/31/23	02/06/23	1330FS*	
1360	Millwork	10	01/31/23	02/13/23	1330FS*	1380FS, 136!
1370	MEP Wall Finishes	10	02/07/23	02/20/23	1340FS-5d*	1390FS*, 140
1365	Ktchen Equipment Installation	5	02/14/23	02/20/23	1360FS*	1380FS*
1380	Countertops	5	02/21/23	02/27/23	1360FS, 1365	
1390	Flooring	15	02/21/23	03/13/23	1370FS*	3920FS, 140(
1400	Doors & Hardware	5	05/16/23	05/22/23	1370FS, 1390	2160FS*
Level 3						
1435	Interior Masonry Walls	20	10/10/22A	11/04/22	1430FS*	1640FS*
1420	Hangers & Top Track	5	11/28/22	12/02/22	1640FS*, 141(	1440FS
1440	Fireproofing	5	12/12/22	12/16/22	1650FS*, 141(	1450FS*
1450	Framing	10	12/19/22	12/30/22	1440FS*	1460FS-5d*
1460	In-Wall MEP Rough-Ins	20	12/26/22	01/20/23	1450FS-5d*	1470FS-3d*
1470	1st Side Drywall	5	01/18/23	01/24/23	1460FS-3d*	1490FS, 148(
1480	Insulation	3	01/23/23	01/25/23	1470FS-2d*	1490FS*
1490	2nd Side Drywall	5	01/26/23	02/01/23	1470FS, 1480	1500FS*
1500	Tape & Finish Walls	8	02/02/23	02/13/23	1490FS*	1510FS*
1510	Paint	5	02/14/23	02/20/23	1500FS*	1520FS*
1520	ACT Grid	5	02/21/23	02/27/23	1510FS*	1530FS*, 155
1530	MEP Ceiling Finishes	10	02/28/23	03/13/23	1520FS*	1560FS-7d*
1540	Interior Glazing	5	02/28/23	03/06/23	1520FS*	
1550	Millwork	10	02/28/23	03/13/23	1520FS*	1570FS-5d*
1560	MEP Wall Finishes	10	03/03/23	03/16/23	1530FS-7d*	1580FS*, 159
1570	Countertops	5	03/07/23	03/13/23	1550FS-5d*	1580FS
1580	Flooring	15	03/17/23	04/06/23	1570FS, 1560	3930FS, 159(
1590	Doors & Hardware	5	06/06/23	06/12/23	1560FS, 1580	2350FS*
Elevator						
1600	Install Elevator Cab	10	03/07/23	03/20/23	1110FS, 2950	1610FS*
1610	Frame & Drywall Around Elevator	10	03/21/23	04/03/23	1600FS*	1620FS*
1620	Install Elevator Finishes	10	04/04/23	04/17/23	1610FS*	1630FS*
1630	Elevator Test	1	04/18/23	04/18/23	1620FS*	
Roofing						
1640	Steel Roof Joists & Metal Decking	15	11/07/22	11/25/22	1430FS, 1435	1650FS*, 142
1650	Roofing	10	11/28/22	12/09/22	1640FS*	1440FS*, 109
Area 11						
Level 1						
2540	1st Side Drywall	5	01/02/23	01/06/23	2530FS-5d, 3(	2560FS, 273(
2550	Insulation	3	01/09/23	01/11/23	2540FS*	2560FS*
2560	2nd Side Drywall	5	01/12/23	01/18/23	2540FS, 2550	2570FS*
2570	Tape & Finish Walls	8	01/19/23	01/30/23	2560FS*	2580FS*
2580	Paint	5	01/31/23	02/06/23	2570FS*	2590FS*

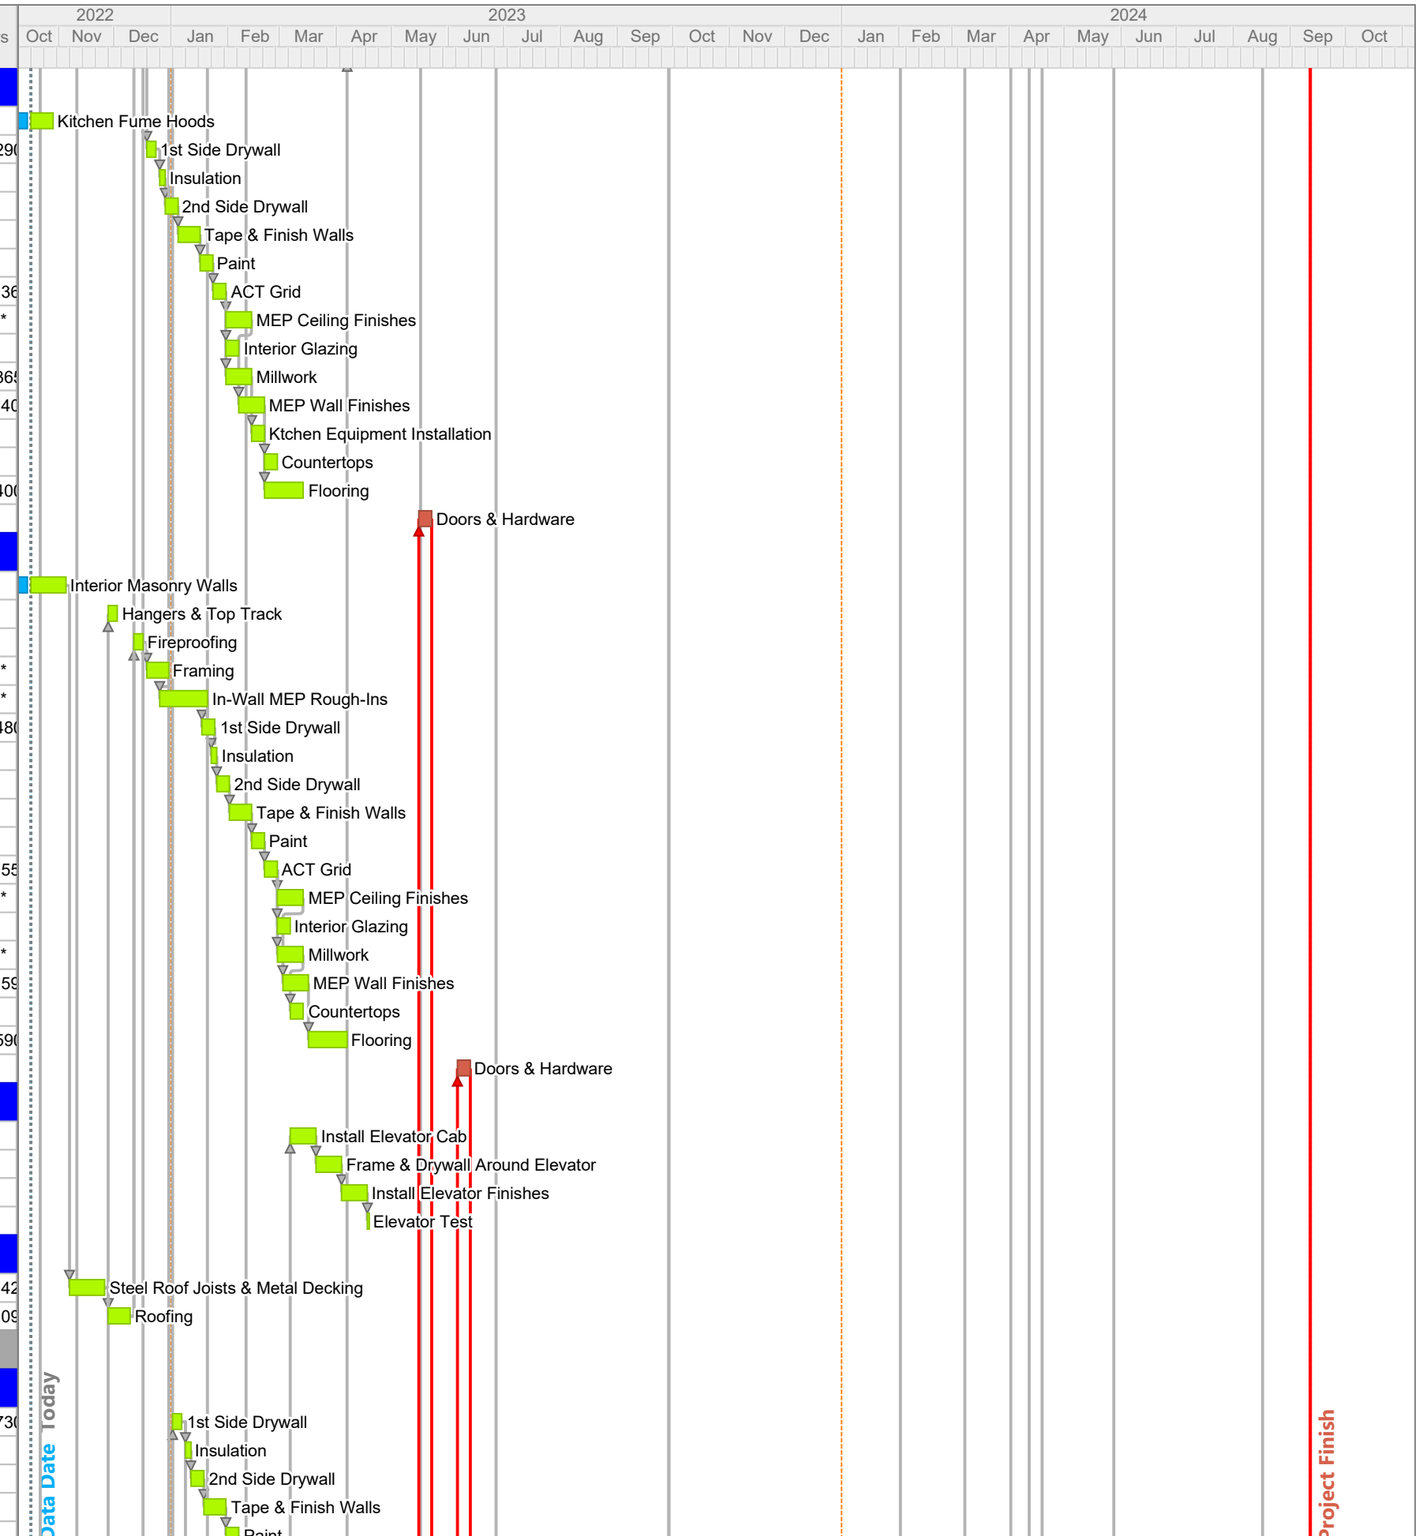

ID	Description	Original Duration	Start	Finish	Predecessors	Successors
2590	ACT Grid	5	02/07/23	02/13/23	2580FS*	2600FS*, 262
2600	MEP Ceiling Finishes	10	02/14/23	02/27/23	2590FS*	2630FS-5d*
2610	Interior Glazing	5	02/14/23	02/20/23	2590FS*	
2620	Millwork	10	02/14/23	02/27/23	2590FS*	2640FS*
2630	MEP Wall Finishes	10	02/21/23	03/06/23	2600FS-5d*	2650FS*, 266
2640	Countertops	5	02/28/23	03/06/23	2620FS*	2650FS*
2650	Flooring	15	03/07/23	03/27/23	2630FS*, 264(	2660FS
2660	Doors & Hardware	5	05/09/23	05/15/23	1970FS*, 263(	1400FS*
Level 2						
2690	Top Track and Hangers	5	10/18/22	10/24/22	2880FS*, 268	2700FS*
2700	Fireproofing	5	10/25/22	10/31/22	2670FS, 2680	2710FS*
2710	Framing	10	11/01/22	11/14/22	2700FS*	2720FS-5d*
2720	In-Wall MEP Rough-Ins	20	11/08/22	12/05/22	2710FS-5d*	2730FS
2730	1st Side Drywall	5	01/09/23	01/13/23	2540FS*, 272(	2750FS, 274(
2740	Insulation	3	01/16/23	01/18/23	2730FS*	2750FS*
2750	2nd Side Drywall	5	01/19/23	01/25/23	2730FS, 2740	2760FS*
2760	Tape & Finish Walls	8	01/26/23	02/06/23	2750FS*	2770FS*
2770	Paint	5	02/07/23	02/13/23	2760FS*	2780FS*
2780	ACT Grid	5	02/14/23	02/20/23	2770FS*	2790FS*, 281
2790	MEP Ceiling Finishes	10	02/21/23	03/06/23	2780FS*	2820FS-5d*
2800	Interior Glazing	5	02/21/23	02/27/23	2780FS*	
2810	Millwork	10	02/21/23	03/06/23	2780FS*	2830FS*
2820	MEP Wall Finishes	10	02/28/23	03/13/23	2790FS-5d*	2840FS*, 285
2830	Countertops	5	03/07/23	03/13/23	2810FS*	2840FS*
2840	Flooring	15	03/14/23	04/03/23	2820FS*, 283(	2850FS
2850	Doors & Hardware	5	05/30/23	06/05/23	2160FS*, 282(	1590FS*
Level 3						
2880	Prep & Pour Slab on Metal Deck	6	10/10/22A	10/17/22	2680FS*, 286(	2890FS, 2690
2870	Hangers & Top Track	5	12/19/22	12/23/22	3050FS*	2890FS
2890	Fireproofing	5	01/02/23	01/06/23	2860FS, 2880	2900FS*
2900	Framing	10	01/09/23	01/20/23	2890FS*	2910FS-5d*,
2910	In-Wall MEP Rough-Ins	20	01/16/23	02/10/23	2900FS-5d*	100FF*, 2920
2920	1st Side Drywall	5	02/08/23	02/14/23	2910FS-3d*	2940FS, 293(
2930	Insulation	3	02/15/23	02/17/23	2920FS*	2940FS-2d*
2940	2nd Side Drywall	5	02/16/23	02/22/23	2920FS, 2930	2950FS*
2950	Tape & Finish Walls	8	02/23/23	03/06/23	2940FS*	2960FS*, 160
2960	Paint	5	03/07/23	03/13/23	2950FS*	2970FS-2d*
2970	ACT Grid	5	03/10/23	03/16/23	2960FS-2d*	2980FS*, 300
2980	MEP Ceiling Finishes	10	03/17/23	03/30/23	2970FS*	3010FS-7d*
2990	Interior Glazing	5	03/17/23	03/23/23	2970FS*	
3000	Millwork	10	03/17/23	03/30/23	2970FS*	3020FS*
3010	MEP Wall Finishes	10	03/22/23	04/04/23	2980FS-7d*	3030FS, 304(
3020	Countertops	5	03/31/23	04/06/23	3000FS*	1210FS*, 303
3030	Flooring	15	04/07/23	04/27/23	3010FS, 3020	3930FS, 386(
3040	Doors & Hardware	5	06/20/23	06/26/23	2350FS*, 301(	110FF*, 3350
Roofing						
3050	Steel Roof Joists & Metal Decking	15	11/28/22	12/16/22	1640FS*, 286(	3060FS*, 287
3055	Precast Stair Install Area 11 & 12	10	12/19/22	12/30/22	3050FS*	
3060	Roofing	10	12/19/22	12/30/22	3050FS*	2540FS*, 289
Area 10						

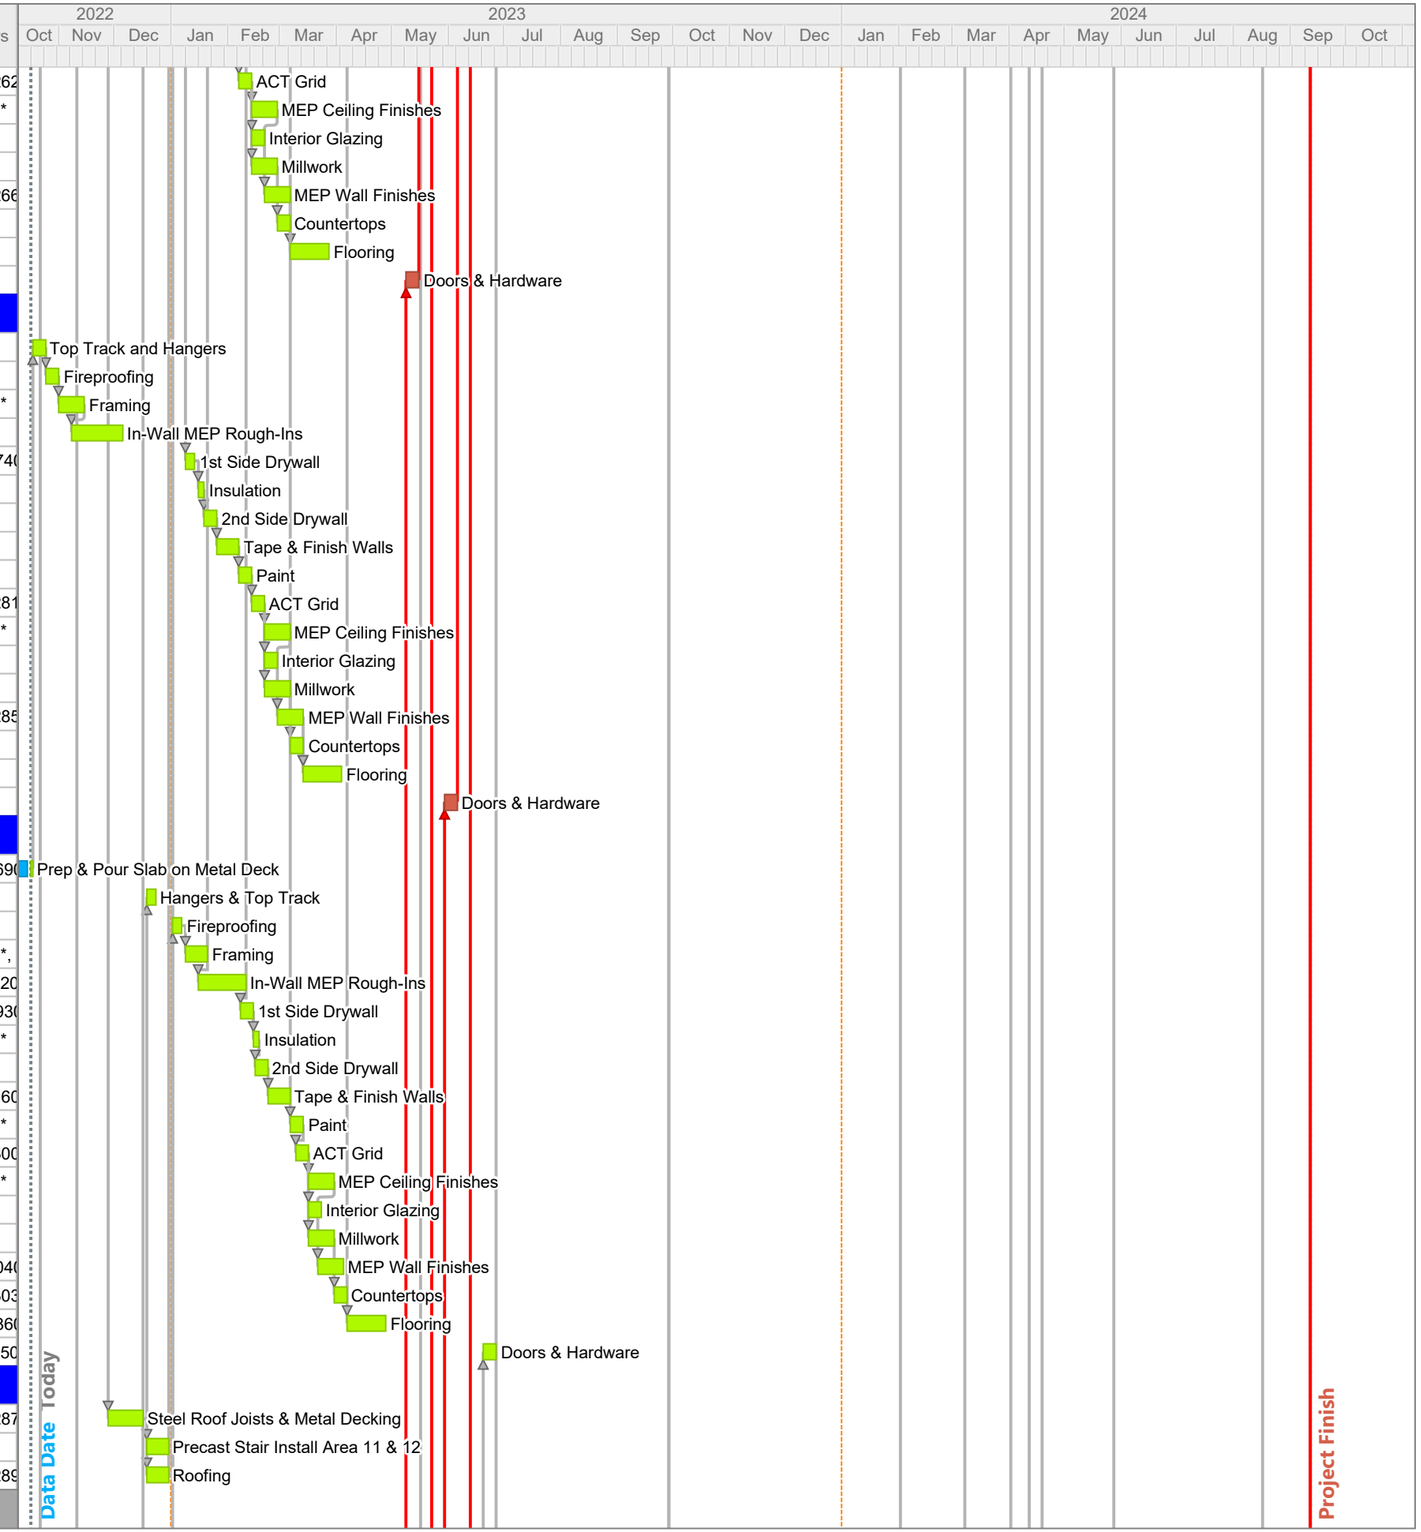

ID	Description	Original Duration	Start	Finish	Predecessors	Successors
Level 1						
3170	Structural Masonry	55	04/04/22A	10/21/22	330FS*	50FF*, 3180F
3180	Structural Steel Level 1 Columns Only	5	10/24/22	10/28/22	1800SS, 2490	3200FS, 336
3190	Top Track and Hangers	5	11/28/22	12/02/22	3370FS*	3200FS*
3200	Fireproofing	5	12/05/22	12/09/22	3180FS, 3190	3210FS*
3210	Framing	10	12/12/22	12/23/22	3200FS*	3220FS-5d*,
3220	MEP Rough-Ins	20	12/19/22	01/13/23	3210FS-5d*	3230FS-5d
3230	1st Side Drywall	5	03/01/23	03/07/23	3220FS-5d, 37	3250FS, 342
3240	Insulation	3	03/08/23	03/10/23	3230FS*	3250FS*
3250	2nd Side Drywall	5	03/13/23	03/17/23	3230FS, 3240	3260FS*
3260	Tape & Finish Walls	8	03/20/23	03/29/23	3250FS*	3270FS*
3270	Paint	5	03/30/23	04/05/23	3260FS*	3280FS*
3280	ACT Grid	5	04/06/23	04/12/23	3270FS*	3290FS*, 331
3290	MEP Ceiling Finishes	10	04/13/23	04/26/23	3280FS*	3320FS-5d*
3300	Interior Glazing	5	04/13/23	04/19/23	3280FS*	
3310	Millwork	10	04/13/23	04/26/23	3280FS*	3330FS*
3320	MEP Wall Finishes	10	04/20/23	05/03/23	3290FS-5d*	3340FS*, 335
3330	Countertops	5	04/27/23	05/03/23	3310FS*	3340FS*
3340	Flooring	15	05/04/23	05/24/23	3320FS*, 333	3350FS
3350	Doors & Hardware	5	06/27/23	07/03/23	3040FS*, 332	3540FS*
Level 2						
3360	Structural Steel Level 2 Beams, Deck & Columns	15	10/31/22	11/18/22	1980FS*, 318	3390FS, 355
3370	Prep & Pour Slab on Metal Deck	5	11/21/22	11/25/22	3360FS*	3390FS, 357
3380	Top Track and Hangers	5	01/09/23	01/13/23	3570FS*	3390FS*
3390	Fireproofing	5	01/16/23	01/20/23	3360FS, 3370	3400FS*
3400	Framing	10	01/23/23	02/03/23	3210FS, 3390	3410FS-5d*,
3410	In-Wall MEP Rough-Ins	20	01/30/23	02/24/23	3400FS-5d*	3420FS
3420	1st Side Drywall	5	03/08/23	03/14/23	3230FS*, 341	3440FS, 343
3430	Insulation	3	03/15/23	03/17/23	3420FS*	3440FS*
3440	2nd Side Drywall	5	03/20/23	03/24/23	3420FS, 3430	3450FS*
3450	Tape & Finish Walls	8	03/27/23	04/05/23	3440FS*	3460FS*
3460	Paint	5	04/06/23	04/12/23	3450FS*	3470FS*
3470	ACT Grid	5	04/13/23	04/19/23	3460FS*	3480FS*, 350
3480	MEP Ceiling Finishes	10	04/20/23	05/03/23	3470FS*	3510FS-5d*
3490	Interior Glazing	5	04/20/23	04/26/23	3470FS*	
3500	Millwork	10	04/20/23	05/03/23	3470FS*	3520FS*
3510	MEP Wall Finishes	10	04/27/23	05/10/23	3480FS-5d*	3530FS*, 354
3520	Countertops	5	05/04/23	05/10/23	3500FS*	3530FS*
3530	Flooring	15	05/11/23	05/31/23	3510FS*, 352	3540FS
3540	Doors & Hardware	5	07/04/23	07/10/23	3350FS*, 351	3730FS*
Level 3						
3550	Structural Steel Level 3 Beams, Deck & Columns	15	12/12/22	12/30/22	1980FS, 2170	3580FS, 374
3570	Prep & Pour Slab on Metal Deck	5	01/02/23	01/06/23	3370FS, 3550	3580FS, 338
3560	Hangers & Top Track	5	02/15/23	02/21/23	3740FS*	3580FS
3580	Fireproofing	5	03/01/23	03/07/23	3550FS, 3570	3590FS*
3590	Framing	10	03/08/23	03/21/23	3400FS, 3580	3600FS-5d*
3600	In-Wall MEP Rough-Ins	20	03/15/23	04/11/23	3590FS-5d*	3610FS*
3610	1st Side Drywall	5	04/12/23	04/18/23	3600FS*	3630FS, 362
3620	Insulation	3	04/19/23	04/21/23	3610FS*	3630FS*
3630	2nd Side Drywall	5	04/24/23	04/28/23	3610FS, 3620	3640FS*
3640	Tape & Finish Walls	8	05/01/23	05/10/23	3630FS*	3650FS*

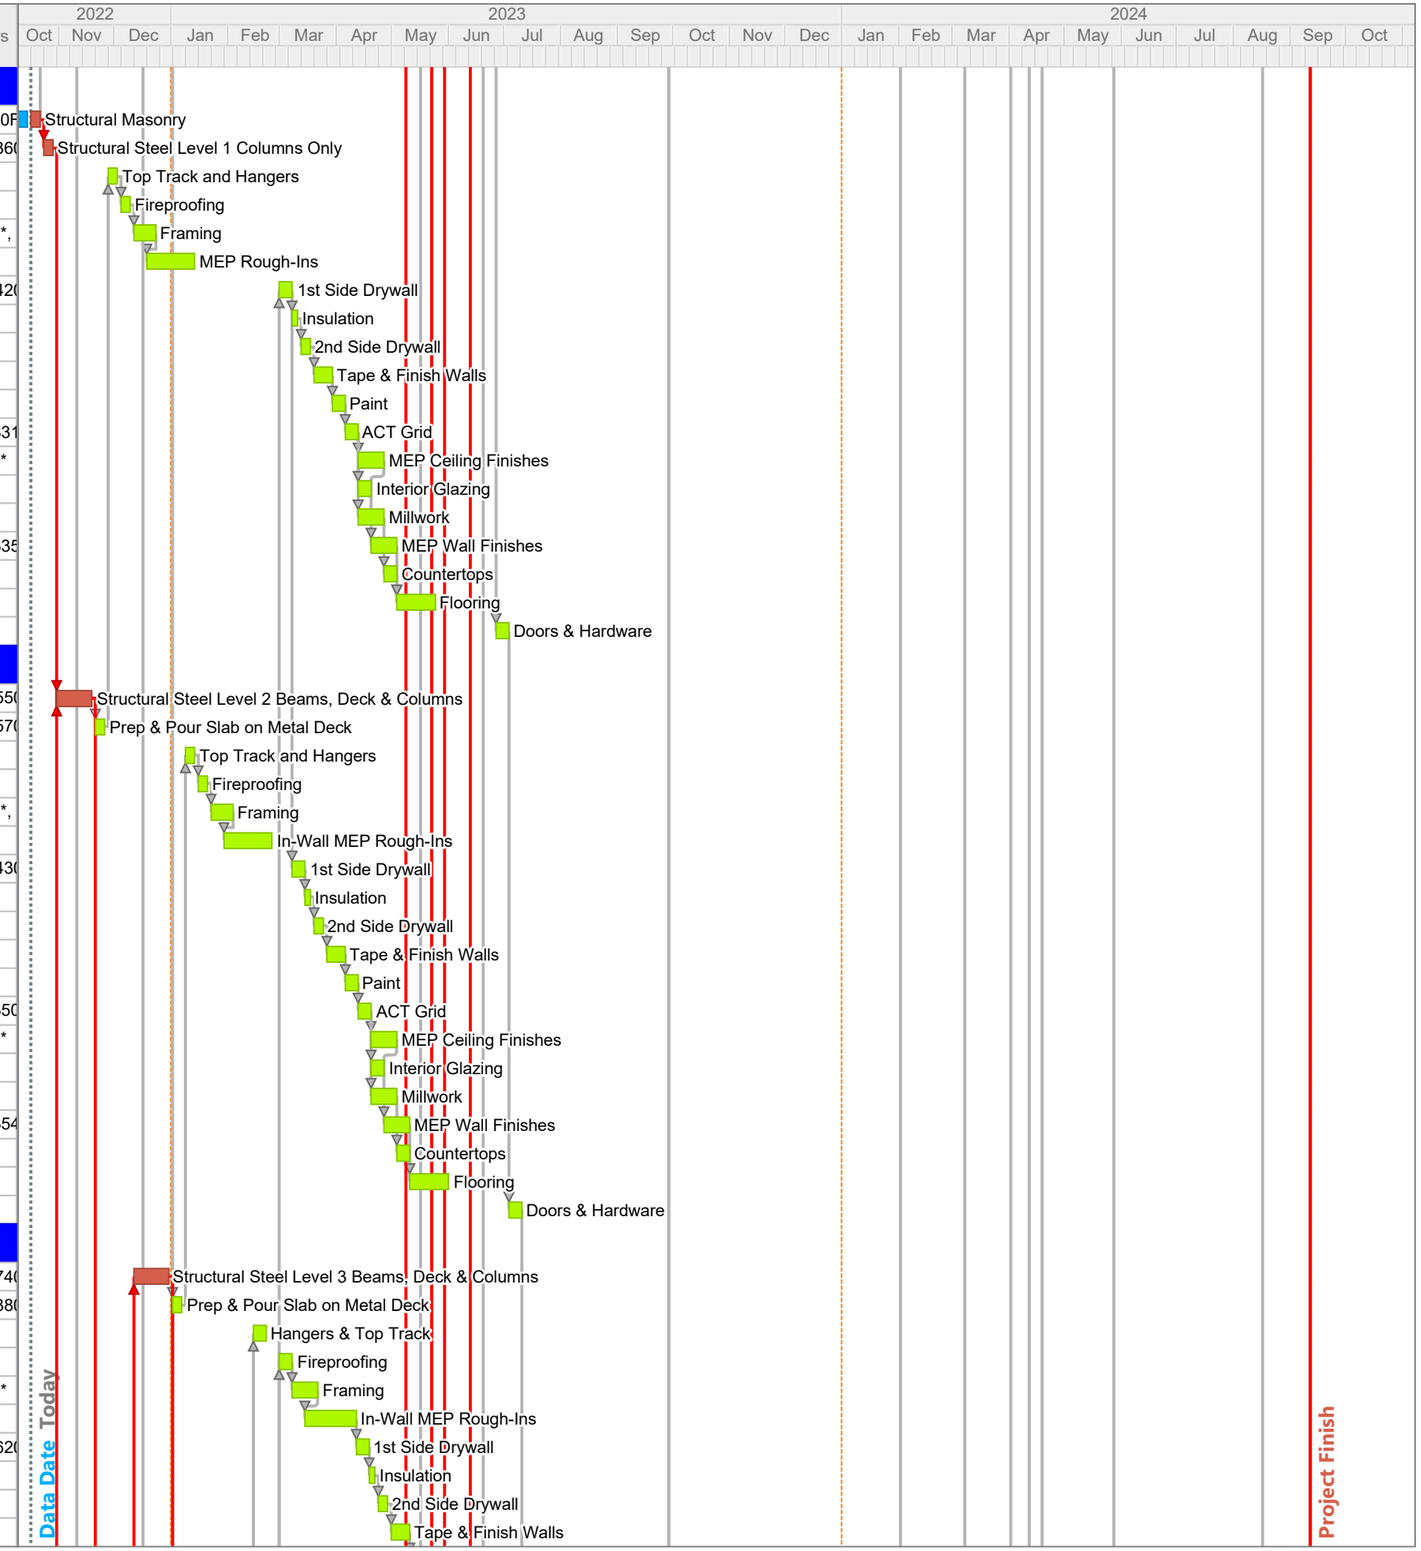

ID	Description	Original Duration	Start	Finish	Predecessors	Successors
3650	Paint	5	05/11/23	05/17/23	3640FS*	3660FS*
3660	ACT Grid	5	05/18/23	05/24/23	3650FS*	3670FS*, 369
3670	MEP Ceiling Finishes	10	05/25/23	06/07/23	3660FS*	3700FS-7d*
3680	Interior Glazing	5	05/25/23	05/31/23	3660FS*	
3690	Millwork	10	05/25/23	06/07/23	3660FS*	3710FS*
3700	MEP Wall Finishes	10	05/30/23	06/12/23	3670FS-7d*	3720FS, 373
3710	Countertops	5	06/08/23	06/14/23	3690FS*	3720FS*
3720	Flooring	15	06/15/23	07/05/23	3700FS, 3710	3860FS*
3730	Doors & Hardware	5	07/11/23	07/17/23	3540FS*, 370	
Roofing						
3740	Steel Roof Joists & Metal Decking	17	01/23/23	02/14/23	2360FS*, 305	3750FS*, 356
3750	Roofing	10	02/15/23	02/28/23	3740FS*	3230FS*, 358
Area 08						
Level 1						
1810	Top Track and Hangers	5	11/07/22	11/11/22	1990FS*	1820FS*
1820	Fireproofing	5	11/14/22	11/18/22	1800FS, 1810	1830FS*
1830	Framing	10	11/21/22	12/02/22	1820FS*	1840FS-5d*
1840	MEP Rough-Ins	20	11/28/22	12/23/22	1830FS-5d*	1850FS-5d
1850	1st Side Drywall	5	02/06/23	02/10/23	1840FS-5d, 2	1870FS, 204
1860	Insulation	3	02/13/23	02/15/23	1850FS*	1870FS*
1870	2nd Side Drywall	5	02/16/23	02/22/23	1850FS, 1860	1880FS*
1880	Tape & Finish Walls	8	02/23/23	03/06/23	1870FS*	1890FS*
1890	Paint	5	03/07/23	03/13/23	1880FS*	1900FS*
1900	ACT Grid	5	03/14/23	03/20/23	1890FS*	1920FS*, 193
1910	Interior Glazing	5	03/21/23	03/27/23	1900FS*	
1920	MEP Ceiling Finishes	10	03/21/23	04/03/23	1900FS*	1940FS-5d*
1930	Millwork	10	03/21/23	04/03/23	1900FS*	1950FS*
1940	MEP Wall Finishes	10	03/28/23	04/10/23	1920FS-5d*	1960FS*, 197
1950	Countertops	5	04/04/23	04/10/23	1930FS*	1960FS*
1960	Flooring	15	04/11/23	05/01/23	1940FS*, 195	1970FS*
1970	Doors & Hardware	5	05/02/23	05/08/23	1210FS, 1940	2660FS*, 235
Level 2						
1980	Structural Steel Level 2 Beams, Deck & Columns	15	10/10/22A	10/28/22	1800FS*	2010FS, 199
1990	Prep & Pour Slab on Metal Deck	5	10/31/22	11/04/22	1980FS*	2010FS, 219
2000	Top Track and Hangers	5	12/19/22	12/23/22	2190FS*	2010FS*
2010	Fireproofing	5	12/26/22	12/30/22	1980FS, 1990	2020FS*
2020	Framing	10	01/02/23	01/13/23	2010FS*	2030FS-5d*
2030	In-Wall MEP Rough-Ins	20	01/09/23	02/03/23	2020FS-5d*	2040FS
2040	1st Side Drywall	5	02/13/23	02/17/23	1850FS*, 203	2060FS, 205
2050	Insulation	3	02/20/23	02/22/23	2040FS*	2060FS*
2060	2nd Side Drywall	5	02/23/23	03/01/23	2040FS, 2050	2070FS*
2070	Tape & Finish Walls	8	03/02/23	03/13/23	2060FS*	2080FS*
2080	Paint	5	03/14/23	03/20/23	2070FS*	2090FS*
2090	ACT Grid	5	03/21/23	03/27/23	2080FS*	2110FS*, 212
2100	Interior Glazing	5	03/28/23	04/03/23	2090FS*	
2110	MEP Ceiling Finishes	10	03/28/23	04/10/23	2090FS*	2130FS-5d*
2120	Millwork	10	03/28/23	04/10/23	2090FS*	2140FS*
2130	MEP Wall Finishes	10	04/04/23	04/17/23	2110FS-5d*	2150FS*, 216
2140	Countertops	5	04/11/23	04/17/23	2120FS*	2150FS*
2150	Flooring	15	04/18/23	05/08/23	2130FS*, 214	2160FS
2160	Doors & Hardware	5	05/23/23	05/29/23	1400FS*, 213	2850FS*

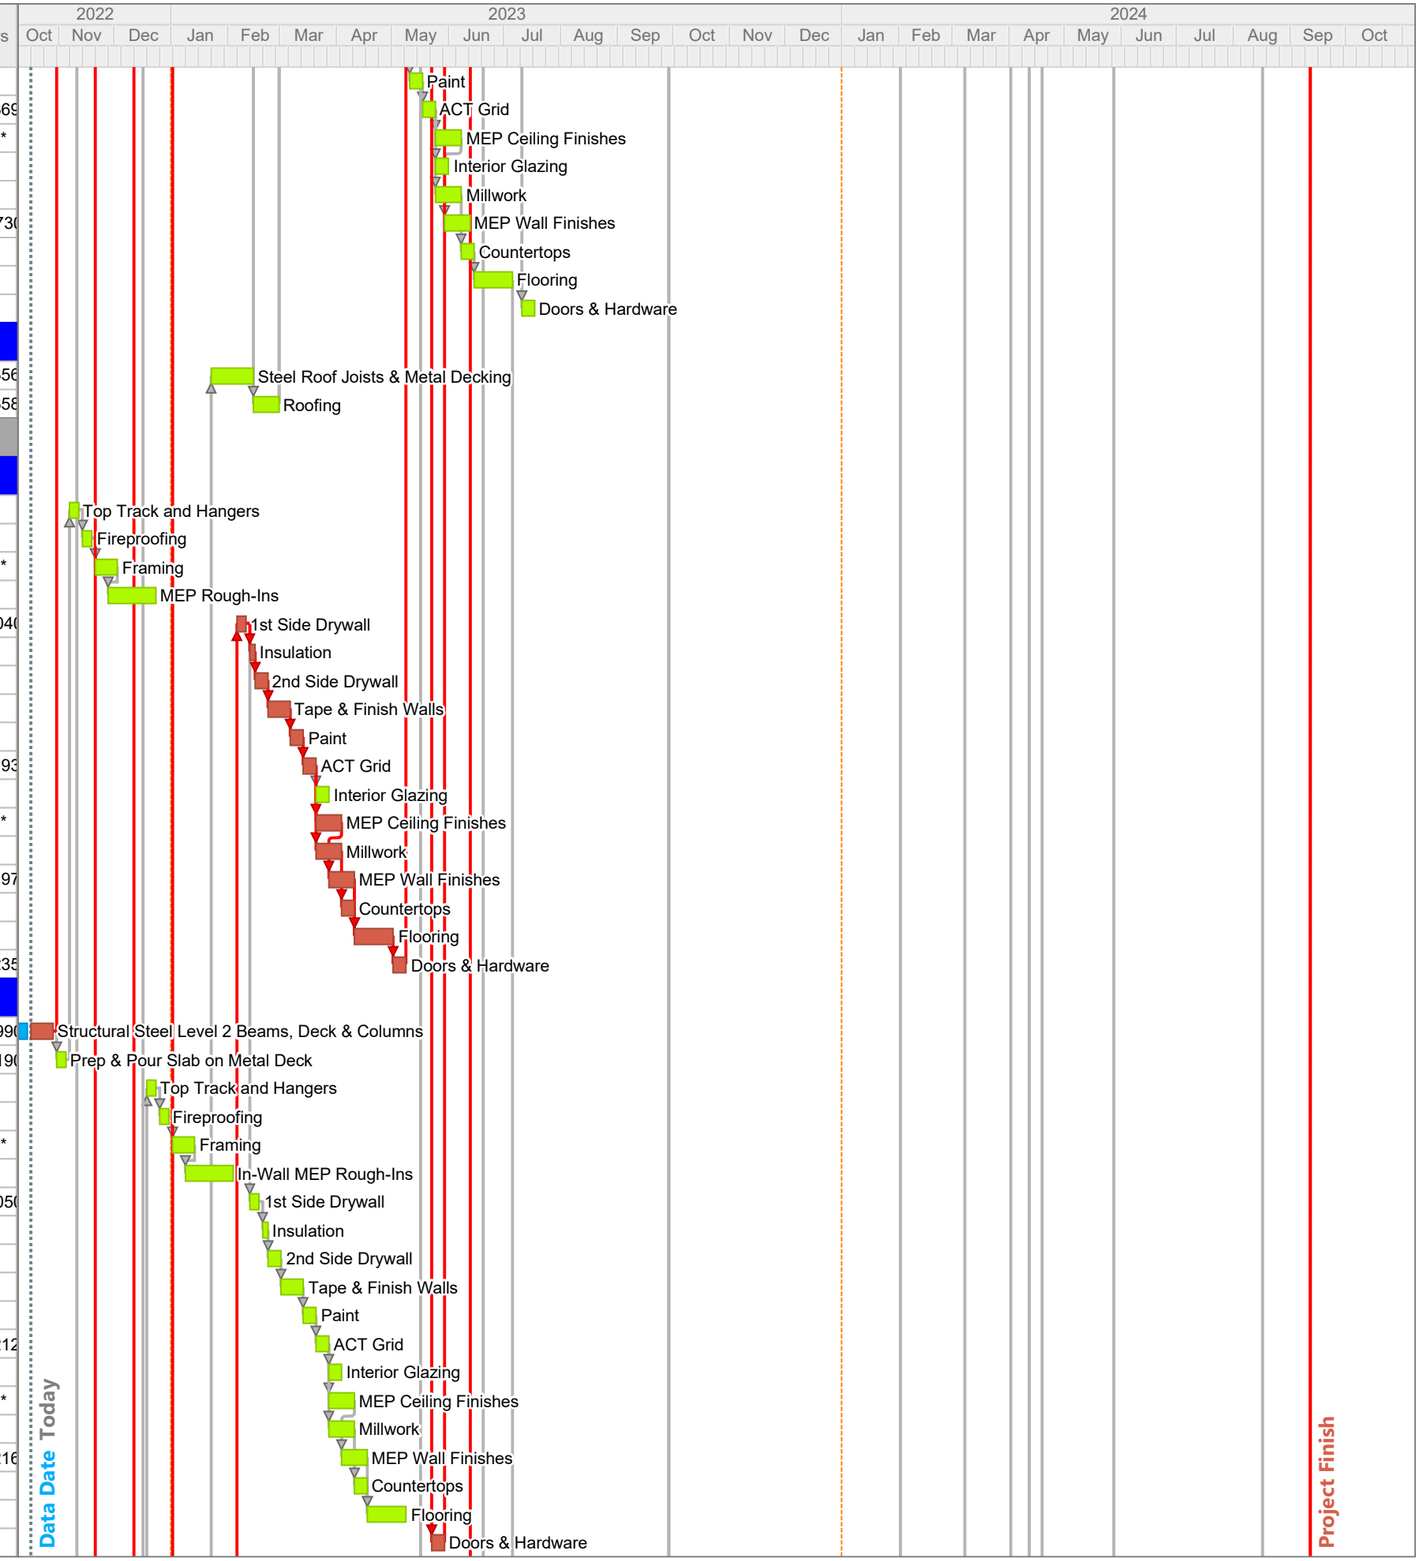

ID	Description	Original Duration	Start	Finish	Predecessors	Successors
Level 3						
2170	Structural Steel Level 3 Beams, Deck & Columns	15	11/21/22	12/09/22	1220FS, 1980	2200FS, 219
2190	Prep & Pour Slab on Metal Deck	5	12/12/22	12/16/22	1990FS, 2170	2200FS, 200
2180	Hangers & Top Track	5	01/23/23	01/27/23	2360FS*	2200FS
2200	Fireproofing	5	02/06/23	02/10/23	2170FS, 2190	2210FS*
2210	Framing	10	02/13/23	02/24/23	2200FS*	2220FS-5d*
2220	In-Wall MEP Rough-Ins	20	02/20/23	03/17/23	2210FS-5d*	2230FS*
2230	1st Side Drywall	5	03/20/23	03/24/23	2220FS*	2250FS, 224
2240	Insulation	3	03/27/23	03/29/23	2230FS*	2250FS*
2250	2nd Side Drywall	5	03/30/23	04/05/23	2230FS, 2240	2260FS*
2260	Tape & Finish Walls	8	04/06/23	04/17/23	2250FS*	2270FS*
2270	Paint	5	04/18/23	04/24/23	2260FS*	2280FS*
2280	ACT Grid	5	04/25/23	05/01/23	2270FS*	2300FS*, 231
2290	Interior Glazing	5	05/02/23	05/08/23	2280FS*	
2300	MEP Ceiling Finishes	10	05/02/23	05/15/23	2280FS*	2320FS-7d*
2310	Millwork	10	05/02/23	05/15/23	2280FS*	2330FS*
2320	MEP Wall Finishes	10	05/05/23	05/18/23	2300FS-7d*	2340FS, 235
2330	Countertops	5	05/16/23	05/22/23	2310FS*	2340FS*
2340	Flooring	15	05/23/23	06/12/23	2320FS, 2330	2350FS*
2350	Doors & Hardware	5	06/13/23	06/19/23	1590FS*, 197	3040FS*, 392
Roofing						
2360	Steel Roof Joists & Metal Decking	15	01/02/23	01/20/23	1410FS, 2170	2370FS*, 218
2365	Precast Stair Install	15	01/23/23	02/10/23	2360FS*	
2370	Roofing	10	01/23/23	02/03/23	2360FS*	1850FS*, 220
Exterior						
3760	Brick Veneer	65	11/21/22	02/17/23	1000FS, 2480	3770FS*, 378
3770	Exterior Framing	20	02/20/23	03/17/23	3760FS*	3810FS*
3780	Exterior Window Frames	15	02/20/23	03/10/23	3760FS*	3790FS*
3790	Field Measure Glazing	2	03/13/23	03/14/23	3780FS*	3800FS*
3800	Procure Glazing	35	03/15/23	05/02/23	3790FS*	3830FS*
3810	Exterior Sheathing	15	03/20/23	04/07/23	3770FS*	3820FS*
3820	Metal Panels	25	04/10/23	05/12/23	3810FS*	3860FS
3830	Install Glazing	10	05/03/23	05/16/23	3800FS*	3860FS, 80F
Sitework						
3765	Snowmelt System Tubing & Concrete Ramp	10	02/20/23	03/03/23	3760FS*	
3860	Final Grading	15	07/06/23	07/26/23	3820FS, 1520	3870FS*
3870	Final Parking Lot Grading	10	07/27/23	08/09/23	3860FS*	3880FS*
3880	Curb & Gutter	15	08/10/23	08/30/23	3870FS*	3890FS*
3890	Paving	2	08/31/23	09/01/23	3880FS*	3910FS, 390
3900	Irrigation & Landscaping	25	09/04/23	10/06/23	3890FS*	3910FS*
3910	Site Punchlist	4	10/09/23	10/12/23	3900FS*, 389	
Phase Closeout						
3920	Construction Clean	40	06/13/23	08/07/23	1200FS, 1390	3930FS*
3930	Westland Punch List	15	08/08/23	08/28/23	1200FS, 3920	3940FS-1d*
3940	Owner Punchlist & Fixes	10	08/28/23	09/08/23	3930FS-1d*	3950FS*
3950	Owner Approval & Move In	14	09/11/23	09/28/23	3940FS*	4890FS, 488
Area 02 - Southeast Athletic Wing						
Phase Closeout						
268	Owner Punchlist & Fixes	10	10/03/22A	11/10/22	4310FS*, 174	417FF*
177	Test & Balance	15	10/07/22A	10/27/22	4305FS*, 205	417FF

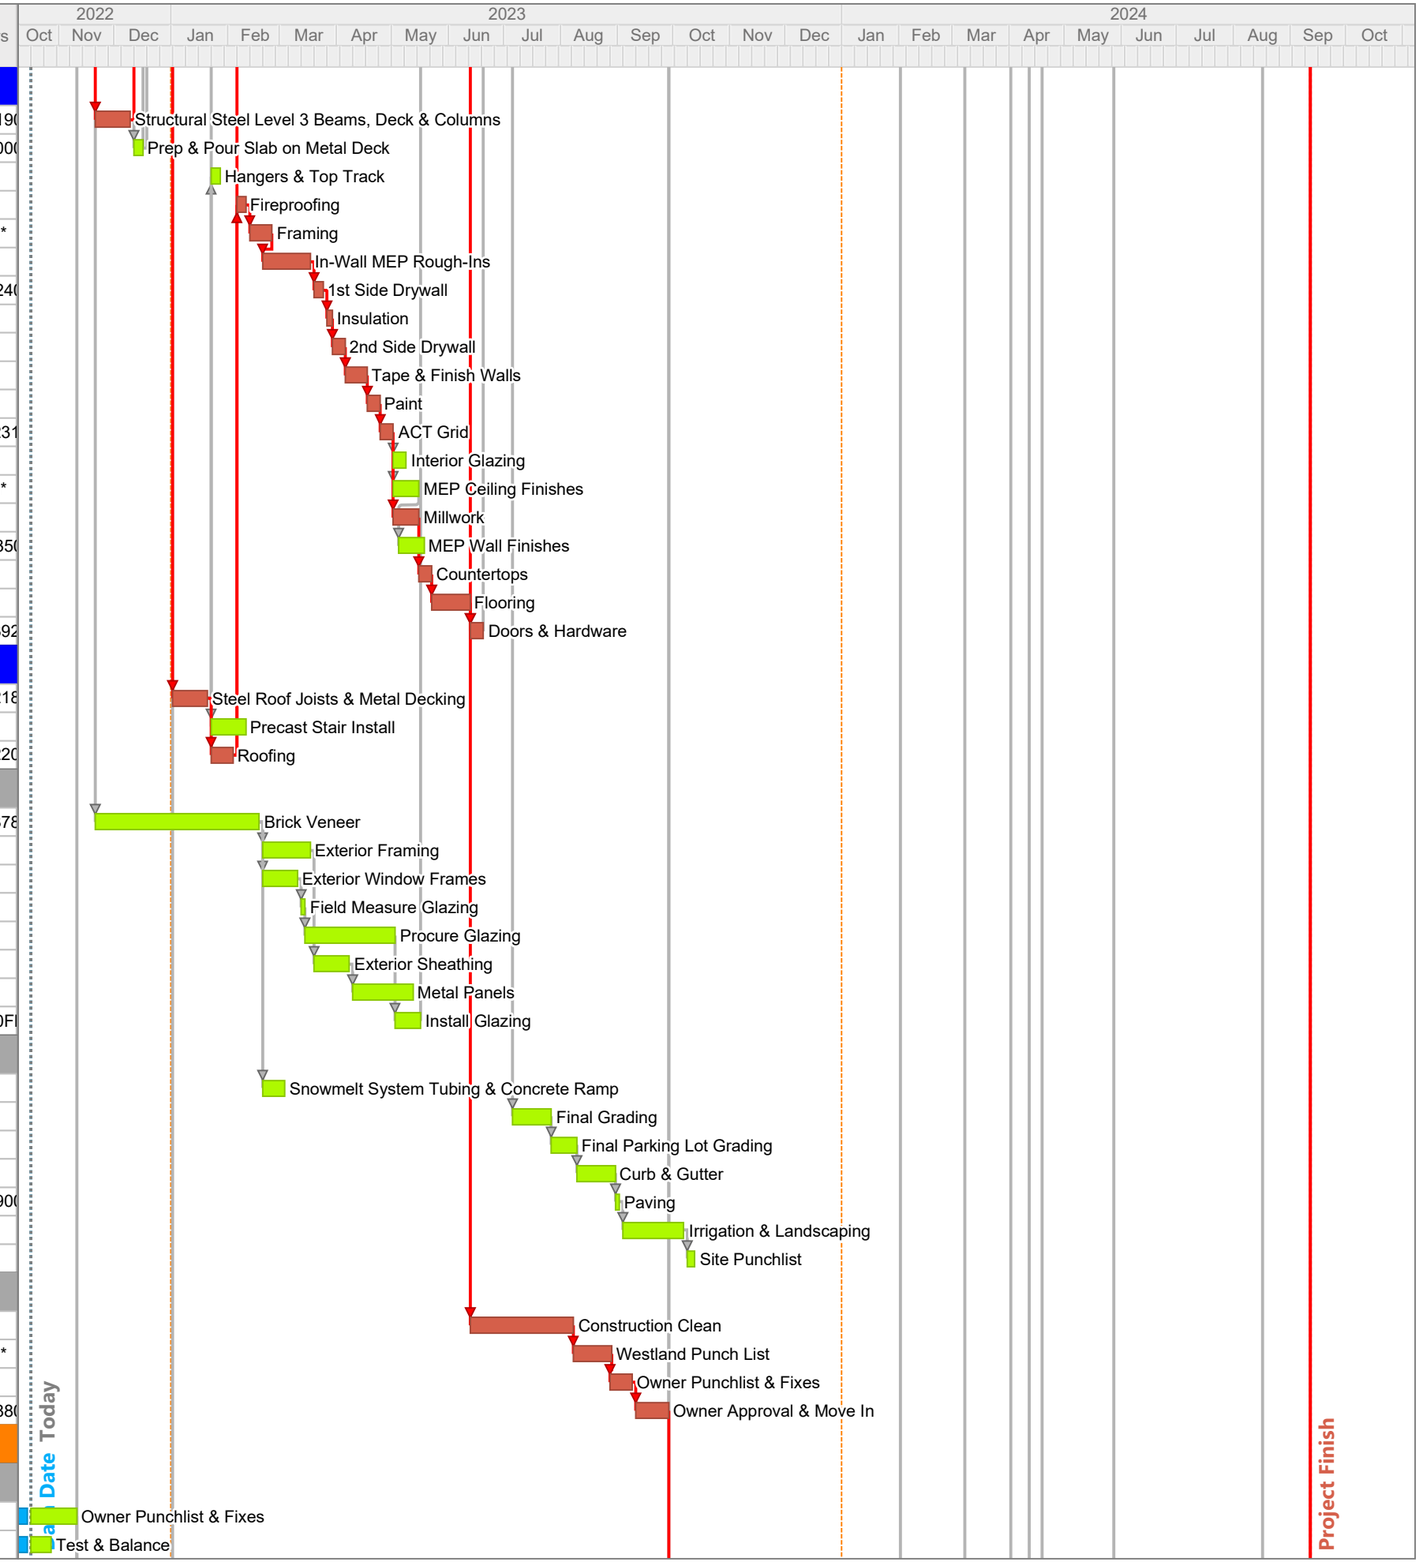

ID	Description	Original Duration	Start	Finish	Predecessors	Successors
178	IMPACT: TOILET PARTITIONS	24	10/10/22A	11/10/22		417FF*
417	Owner Approval & Move In	0		11/10/22	268FF*, 177F	22FF, 25FF*
CTE Wing Remodel						
Level 1 - Wrestling/Dance/Cardio						
4690	Demo	5	01/02/23	01/06/23	1110FS-4d*	4700FS*
4700	Framing	10	01/09/23	01/20/23	4690FS*	4710FS*
4710	MEP Rough-Ins	15	01/23/23	02/10/23	4700FS*	4720FS*
4720	Insulation & 1st Side Drywall	5	02/13/23	02/17/23	4710FS*	4730FS*
4730	2nd Side Drywall	5	02/20/23	02/24/23	4720FS*	4740FS*
4740	Tape & Finish Walls	10	02/27/23	03/10/23	4730FS*	4750FS*
4750	Paint	5	03/13/23	03/17/23	4740FS*	4760FS*
4760	ACT Grid	5	03/20/23	03/24/23	4750FS*	4770FS*, 479
4770	MEP Ceiling Finishes	10	03/27/23	04/07/23	4760FS*	4800FS-5d*
4780	Interior Glazing	10	03/27/23	04/07/23	4760FS*	
4790	Millwork	10	03/27/23	04/07/23	4760FS*	4810FS*
4800	MEP Wall Finishes	10	04/03/23	04/14/23	4770FS-5d*	4830FS, 482
4810	Countertops	2	04/10/23	04/11/23	4790FS*	
4820	Doors & Hardware	5	04/17/23	04/21/23	4800FS*	4830FS*
4830	Flooring	5	04/24/23	04/28/23	4800FS, 4820	4840FS*, 485
Phase Closeout						
4840	Construction Clean	10	05/01/23	05/12/23	4830FS*	4860FS
4850	Westland Punch List	15	05/01/23	05/19/23	4830FS*	4860FS*
4860	Owner Punchlist & Fixes	5	05/22/23	05/26/23	4850FS*, 484	4870FF*
4870	Owner Approval & Move In	0		05/26/23	4860FF*	
SW Wing, No. Aux Gym, Wrestling Replacement						
Demo						
4880	Demo SW Classrooms	30	09/29/23	11/09/23	3950FS*	4890FS*, 519
New Gym Construction						
Concrete & Structure						
4890	Structural Fill & Helical Piers	20	11/10/23	12/07/23	3950FS, 4880	4900FS*
4900	Excavate Footings	5	12/08/23	12/14/23	4890FS*	4910FS*
4910	F/R/P Footings	10	12/15/23	12/28/23	4900FS*	4920SS*, 493
4920	Sub Rough Electrical & Plumbing	10	12/15/23	12/28/23	4910SS*	
4930	F/R/P Foundation Walls	15	12/22/23	01/11/24	4910FS-5d*	4940FS-5d*,
4940	Waterproof Foundation Walls	5	01/05/24	01/11/24	4930FS-5d*	4960FS*
4950	Backfill & Compact Interior Footings	5	01/12/24	01/18/24	4930FS*	4970FS*
4960	Backfill Foundations	5	01/12/24	01/18/24	4940FS*	
4970	Install Vapor Barrier	5	01/19/24	01/25/24	4950FS*	4980FS*
4980	Install Gravel for SOG	3	01/26/24	01/30/24	4970FS*	4990FS*
4990	F/R/P SOG	3	01/31/24	02/02/24	4980FS*	5000FS*
5000	Structural Masonry	50	02/05/24	04/12/24	4990FS*	5010FS-5d*
5010	Structural Steel	10	04/08/24	04/19/24	5000FS-5d*	5020FS-5d*
5020	Metal Roof Decking	10	04/15/24	04/26/24	5010FS-5d*	5170FS*, 518
Interior Finishes						
5030	Paint Gym	7	04/29/24	05/07/24	5020FS*	5050FS*, 506
5040	Roof Drain Lines	10	05/08/24	05/21/24	5170FS, 5030	
5050	Electrical Install	20	05/08/24	06/04/24	5020FS, 5030	5090FF*
5060	Fire Sprinkler Install	10	05/08/24	05/21/24	5020FS, 5030	
5070	Mechanical Install	15	05/08/24	05/28/24	5020FS, 5030	

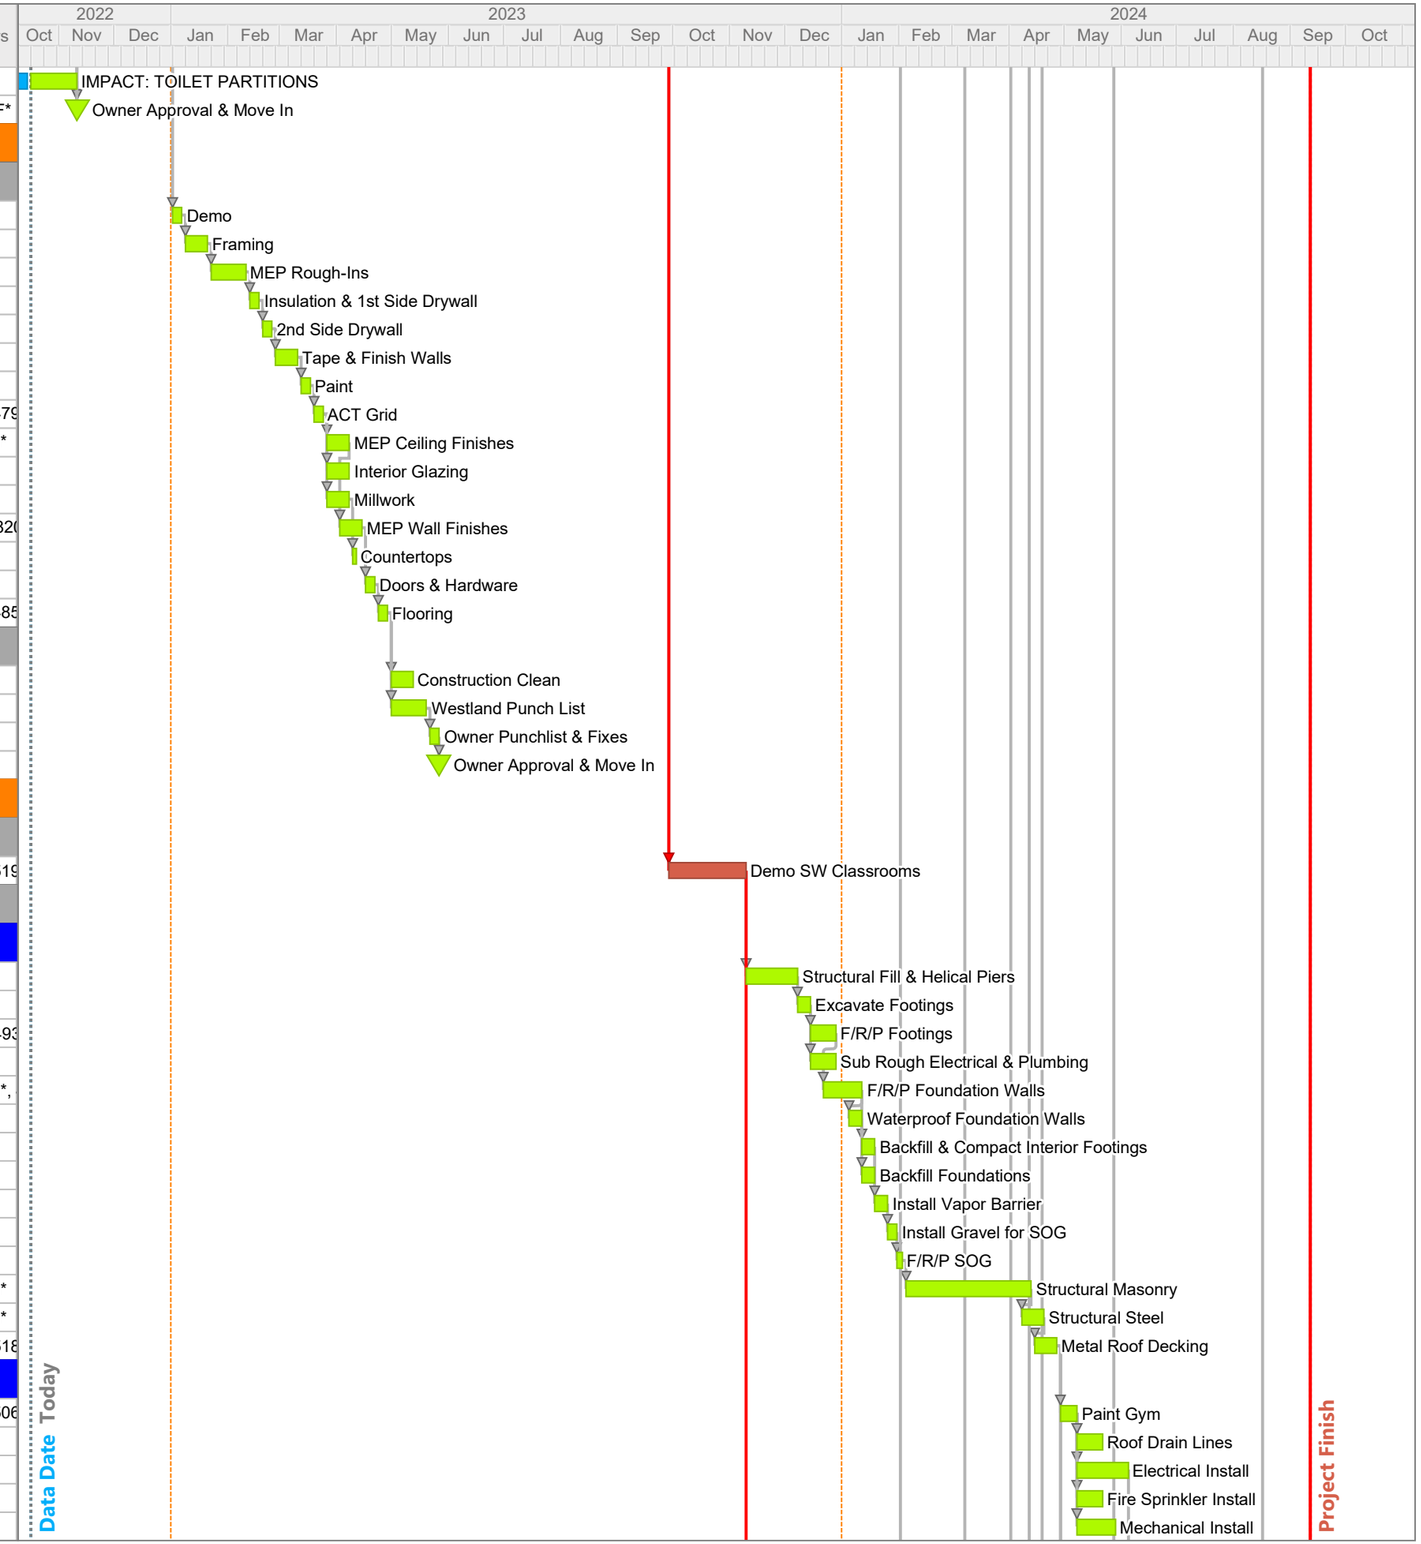

ID	Description	Original Duration	Start	Finish	Predecessors	Successors
5080	Install Doors & Hardware	2	05/20/24	05/21/24	5180FS*	
5090	Wood Floor Acclimation	7	05/27/24	06/04/24	5050FF*	5100FS*
5100	Install Basketball Standards	3	06/05/24	06/07/24	5090FS*	5110FS*
5110	Wood Floor Install	15	06/10/24	06/28/24	5100FS*	5120FS-8d*,
5120	Install Bleachers	8	06/19/24	06/28/24	5110FS-8d*	
5130	Construction Clean	3	07/01/24	07/03/24	5110FS*	5140FS*
5140	Punch List & Fixes	5	07/04/24	07/10/24	5130FS*	5150FS*
5150	Final Inspections	1	07/11/24	07/11/24	5140FS*	5160FS*
5160	Final Clean	3	07/12/24	07/16/24	5150FS*	
Roofing						
5170	Install Roof Drains	5	04/29/24	05/03/24	5020FS*	5040FS
5180	Roofing	15	04/29/24	05/17/24	5020FS*	5080FS*
Level 1 - Wrestling/Dance/Cardio						
Concrete & Structure						
5190	Excavate Footings	5	11/10/23	11/16/23	4880FS*	5200FS*
5200	F/R/P Footings	10	11/17/23	11/30/23	5190FS*	5210SS*, 522
5210	Sub Rough Electrical & Plumbing	8	11/17/23	11/28/23	5200SS*	5260FS
5220	F/R/P Foundation Walls	10	11/24/23	12/07/23	5200FS-5d*	5230FS-5d*,
5230	Waterproof Foundation Walls	5	12/01/23	12/07/23	5220FS-5d*	5240FS*
5240	Backfill Foundations	5	12/08/23	12/14/23	5230FS*	5260FS*
5250	Backfill & Compact Interior Footings	5	12/08/23	12/14/23	5220FS*	5260FS*
5260	Install Vapor Barrier	2	12/15/23	12/18/23	5210FS, 5240	5270FS*
5270	Install Gravel for SOG	2	12/19/23	12/20/23	5260FS*	5280FS*
5280	F/R/P SOG	1	12/21/23	12/21/23	5270FS*	5290FS*
5290	Structural Masonry	30	12/22/23	02/01/24	5280FS*	5300FS-8d*,
5300	Structural Steel Level 1 Columns	10	01/23/24	02/05/24	5290FS-8d*	5470FS*, 531
MEP Rough-Ins & Framing						
5310	MEP Above Ceiling Rough-Ins	10	03/08/24	03/21/24	5300FS, 5480	5500FS*, 532
5320	Framing	10	03/15/24	03/28/24	5310FS-5d*	5330FS-5d*
5330	In-Wall MEP Rough-Ins	10	03/22/24	04/04/24	5320FS-5d*	5340FS*
Interior Finishes						
5340	Insulation & 1st Side Drywall	8	04/05/24	04/16/24	5330FS*, 5670	5350FS*, 553
5350	2nd Side Drywall	8	04/17/24	04/26/24	5340FS*	5360FS*
5360	Tape & Finish Walls	15	04/29/24	05/17/24	5350FS*	5370FS*
5370	Paint	10	05/20/24	05/31/24	5360FS*	5380FS*
5380	ACT Grid	10	06/03/24	06/14/24	5370FS*	5390FS*, 541
5390	MEP Ceiling Finishes	15	06/17/24	07/05/24	5380FS*	5430FS-5d*
5400	Interior Glazing	10	06/17/24	06/28/24	5380FS*	
5410	Millwork	5	06/17/24	06/21/24	5380FS*	5420FS*
5420	Countertops	5	06/24/24	06/28/24	5410FS*	
5430	MEP Wall Finishes	10	07/01/24	07/12/24	5390FS-5d*	5460FS, 5440
5440	Doors & Hardware	5	07/15/24	07/19/24	5430FS*	5460FS, 5450
5450	ACT Tiles	5	07/22/24	07/26/24	5380FS, 5440	5460FS*
5460	Flooring	10	07/29/24	08/09/24	5430FS, 5440	
Level 2 - Wrestling/Dance/Cardio						
Concrete & Structure						
5470	Structural Steel Level 2	10	02/06/24	02/19/24	5300FS*	5660FS*, 549
5480	Prep & Pour Slab on Metal Deck	3	03/05/24	03/07/24	5660FS*	5490FS*, 531
5490	Fireproofing	8	03/08/24	03/19/24	5470FS, 5480	5500FS

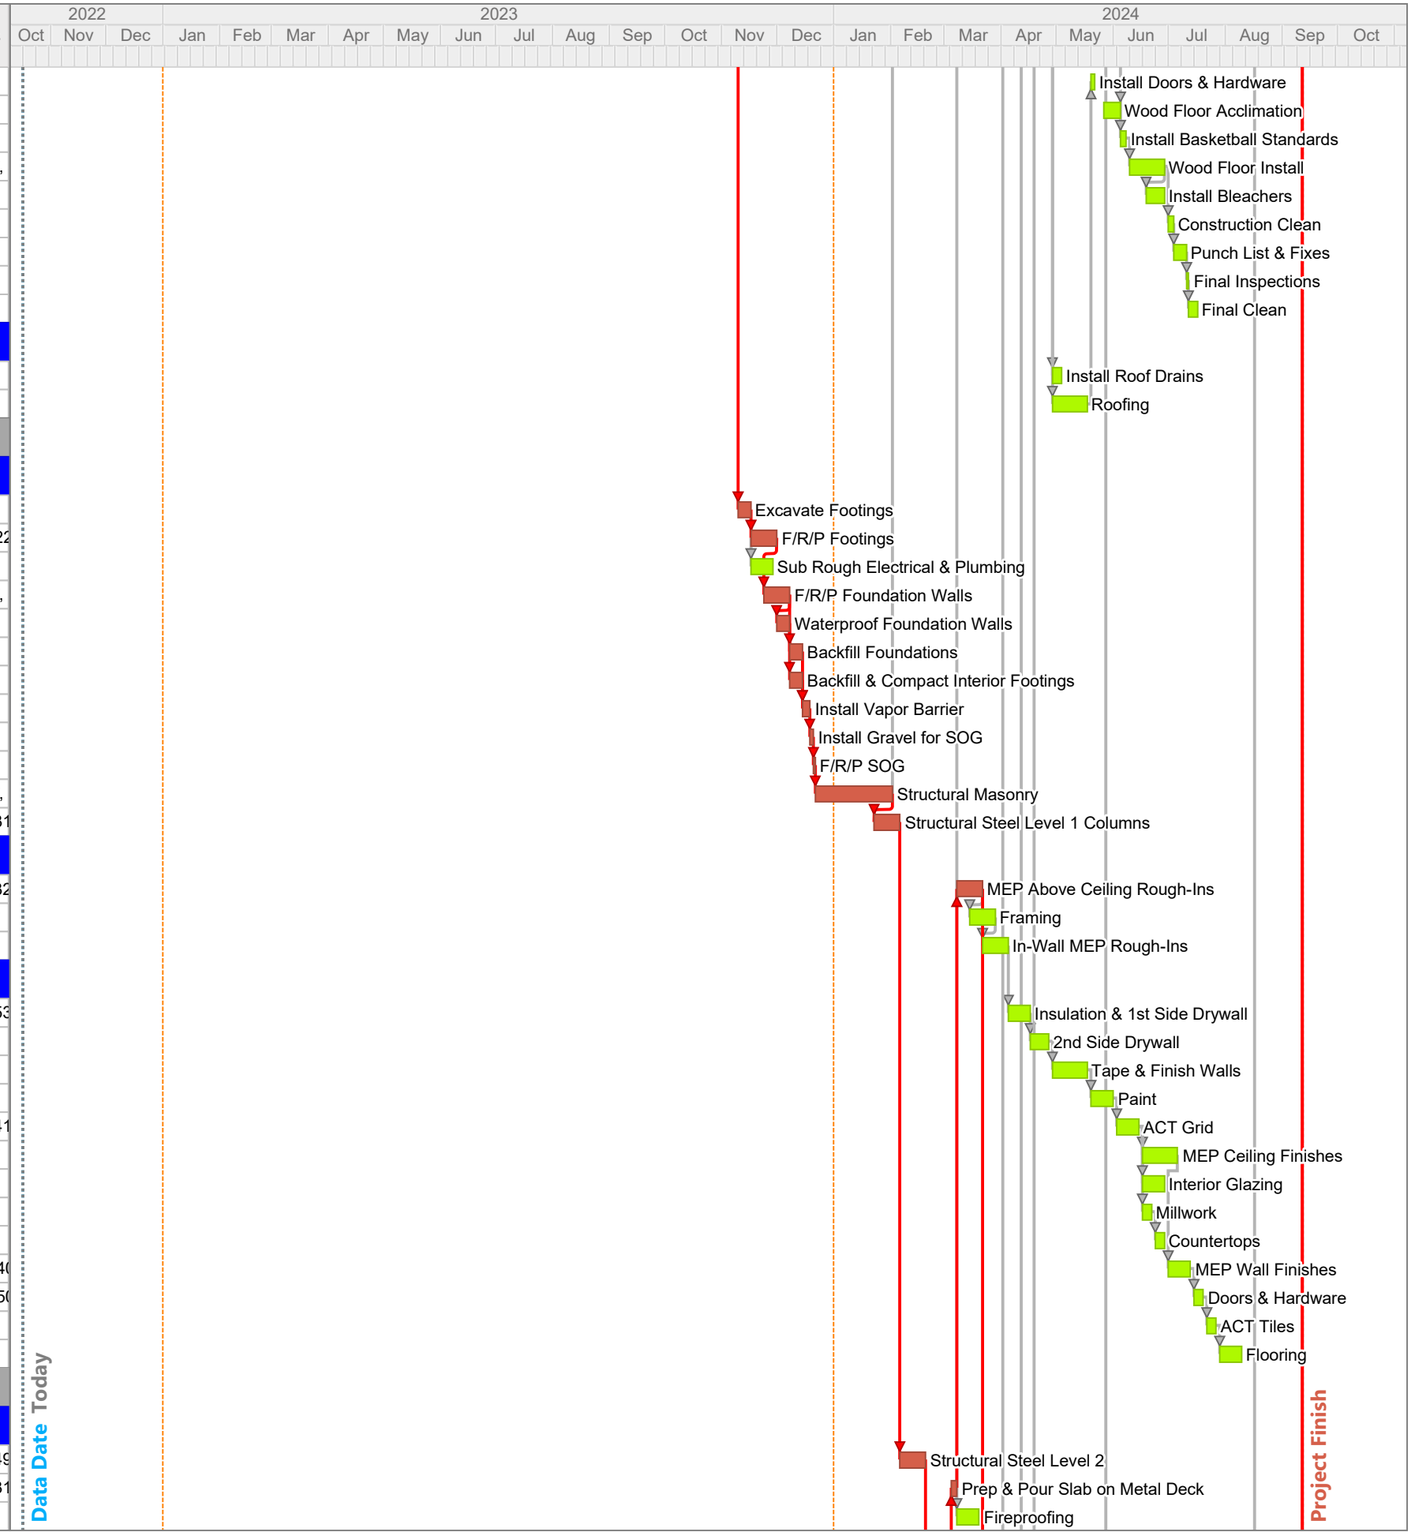

ID	Description	Original Duration	Start	Finish	Predecessors	Successors
MEP Rough-Ins & Framing						
5500	MEP Above Ceiling Rough-Ins	10	03/22/24	04/04/24	5310FS*, 5490	5510FS-5d*
5510	Framing	10	03/29/24	04/11/24	5500FS-5d*	5520FS-5d*,
5520	In-Wall MEP Rough-Ins	10	04/05/24	04/18/24	5510FS-5d*	5530FS*, 190
Interior Finishes						
5530	Insulation & 1st Side Drywall	8	04/19/24	04/30/24	5340FS, 5520	5540FS*
5540	2nd Side Drywall	8	05/01/24	05/10/24	5530FS*	5550FS*
5550	Tape & Finish Walls	15	05/13/24	05/31/24	5540FS*	5560FS*
5560	Paint	10	06/03/24	06/14/24	5550FS*	5570FS*
5570	ACT Grid	10	06/17/24	06/28/24	5560FS*	5580FS*, 560
5580	MEP Ceiling Finishes	15	07/01/24	07/19/24	5570FS*	5610FS-5d*
5590	Interior Glazing	15	07/01/24	07/19/24	5570FS*	
5600	Millwork	10	07/01/24	07/12/24	5570FS*	5620FS*
5610	MEP Wall Finishes	10	07/15/24	07/26/24	5580FS-5d*	5650FS, 5640
5620	Countertops	5	07/15/24	07/19/24	5600FS*	5630FS*, 573
5630	ACT Tiles	5	07/22/24	07/26/24	5570FS, 5620	5650FS
5640	Doors & Hardware	5	07/29/24	08/02/24	5610FS*	5650FS*
5650	Flooring	10	08/05/24	08/16/24	5610FS, 5640	5750FS*, 210
Roofing						
5660	Steel Roof Joists & Metal Decking	10	02/20/24	03/04/24	5470FS*	5670FS*, 548
5670	Roofing	20	03/05/24	04/01/24	5660FS*	5340FS, 170
Exterior						
5680	Brick Veneer	20	03/05/24	04/01/24	5660FS*	5700FS*, 569
5690	Exterior Glazing	10	04/02/24	04/15/24	5680FS*	
5700	Exterior Framing	15	04/02/24	04/22/24	5680FS*	5710FS*, 587
5710	Exterior Sheathing	10	04/23/24	05/06/24	5700FS*	5720FS*
5720	Metal Panels	15	05/07/24	05/27/24	5710FS*	200FF*, 5920
Phase Closeout						
5730	Construction Clean	5	07/22/24	07/26/24	5620FS*	5740SS*
5740	Westland Punch List	10	07/22/24	08/02/24	5730SS*	5750FS, 592
5750	Owner Punchlist & Fixes	18	08/19/24	09/11/24	5650FS*, 574	5760FF*
5760	Owner Approval & Move In	0		09/11/24	5750FF*, 5930	10FF, 20FF*,
Pavillion & South Road Landscaping						
5775	IMPACT: PR #27 - SOUTH ROAD ISSUES	35	10/07/21A	10/28/22		5770FS*
5770	Pavillion & South Road Landscaping	40	10/31/22	12/23/22	5775FS*	
Stadium Seating & Concessions						
5790	Demo/Sitework/Utilities	40	10/17/22A	12/09/22		5800FS*, 581
5780	Cell Tower Relocation	0		11/22/22		
5800	Masonry Building Foundations	20	12/12/22	01/06/23	5790FS*	5820FS*
5810	Bleacher Foundations	20	12/12/22	01/06/23	5790FS*	5830FS*
5820	Masonry	20	01/09/23	02/03/23	5800FS*	5840FS*
5830	Bleacher Structure & Finishs	40	01/09/23	03/03/23	5810FS*	5850FS*
5840	Building Envelope	20	02/06/23	03/03/23	5820FS*	5850FS*
5850	Building Interiors	20	03/06/23	03/31/23	5840FS*, 5830	5860FS*, 595
5860	Commissioning/Punch/Turnover	20	04/03/23	04/28/23	5850FS*	
West Parking Lots						
5870	Final Grading	5	04/23/24	04/29/24	5700FS*	5880FS*
5880	Underground Utilities	15	04/30/24	05/20/24	5870FS*	5890FS*
5890	Curb & Gutter	10	05/21/24	06/03/24	5880FS*	5900FS*

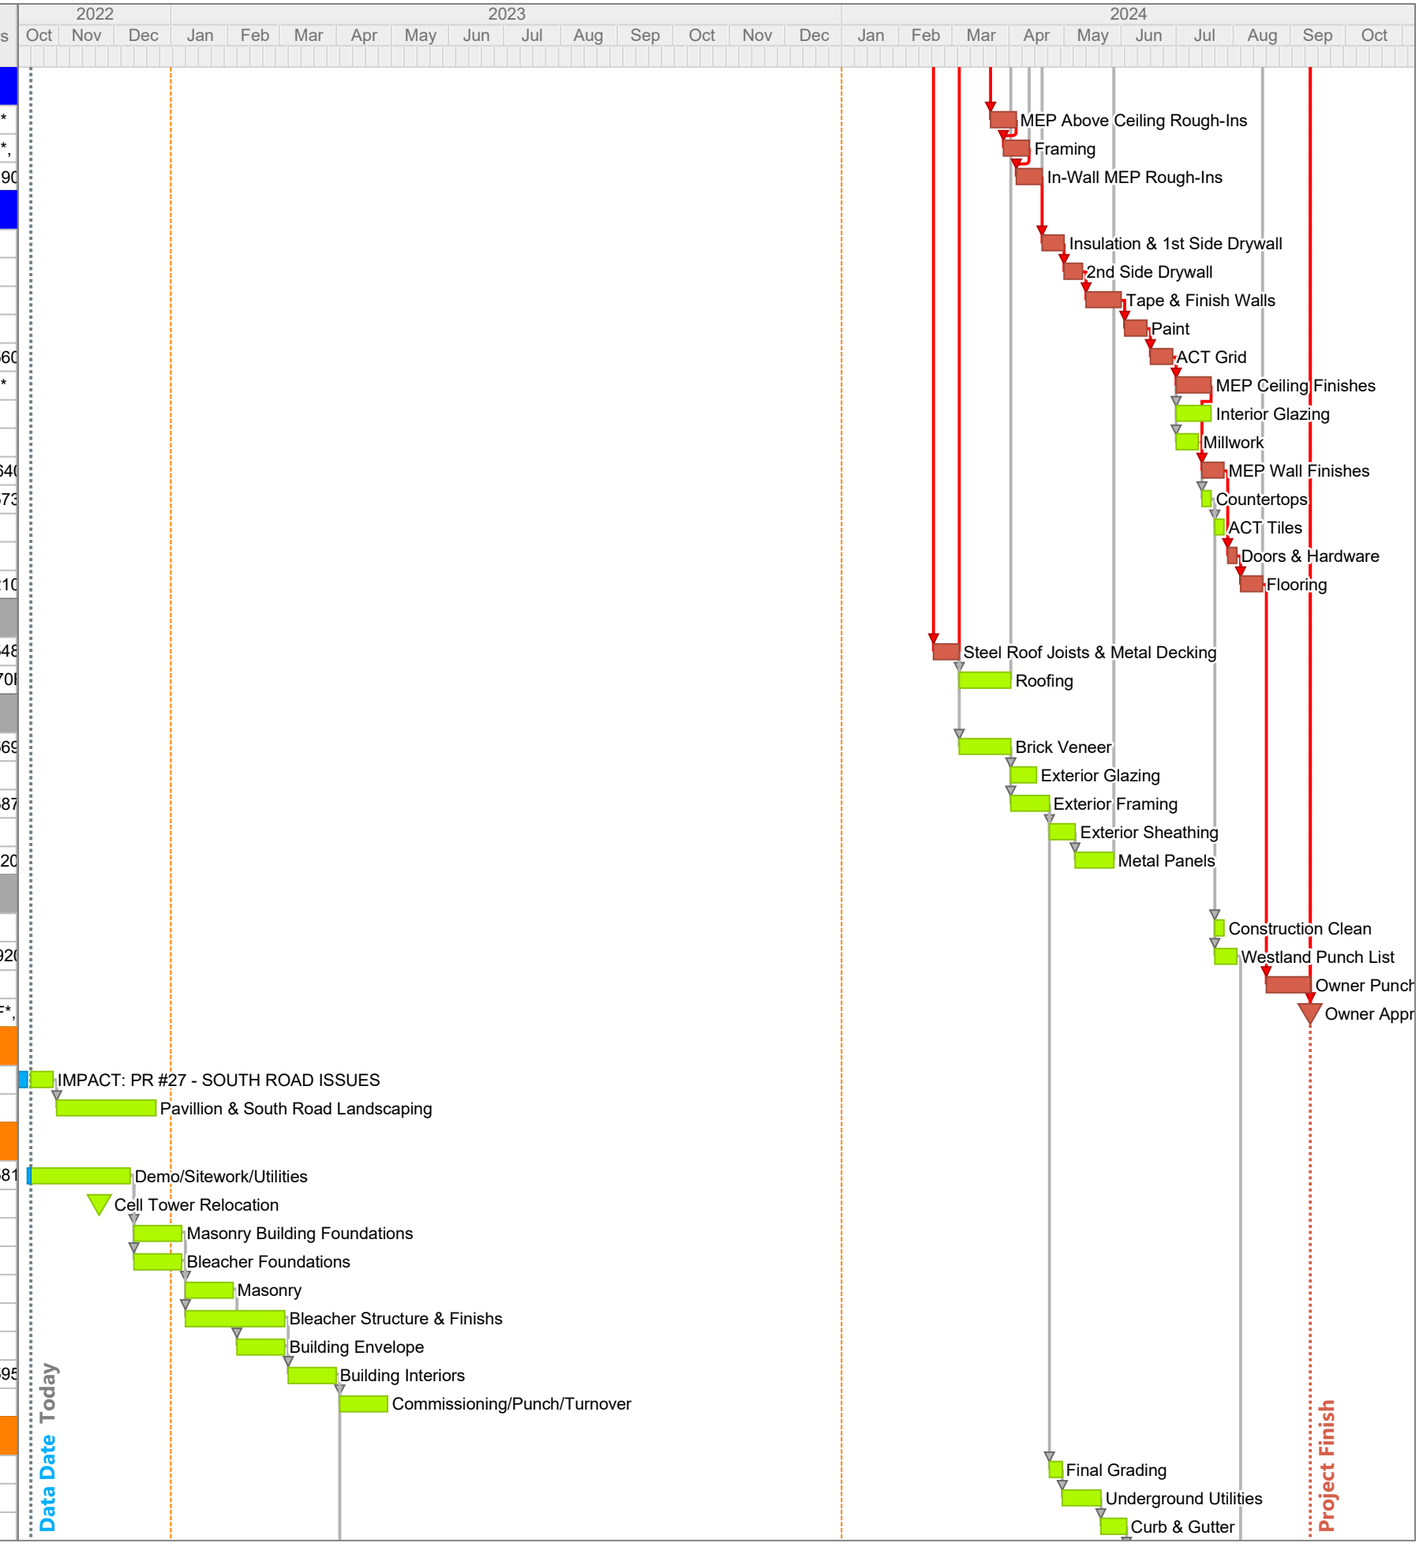
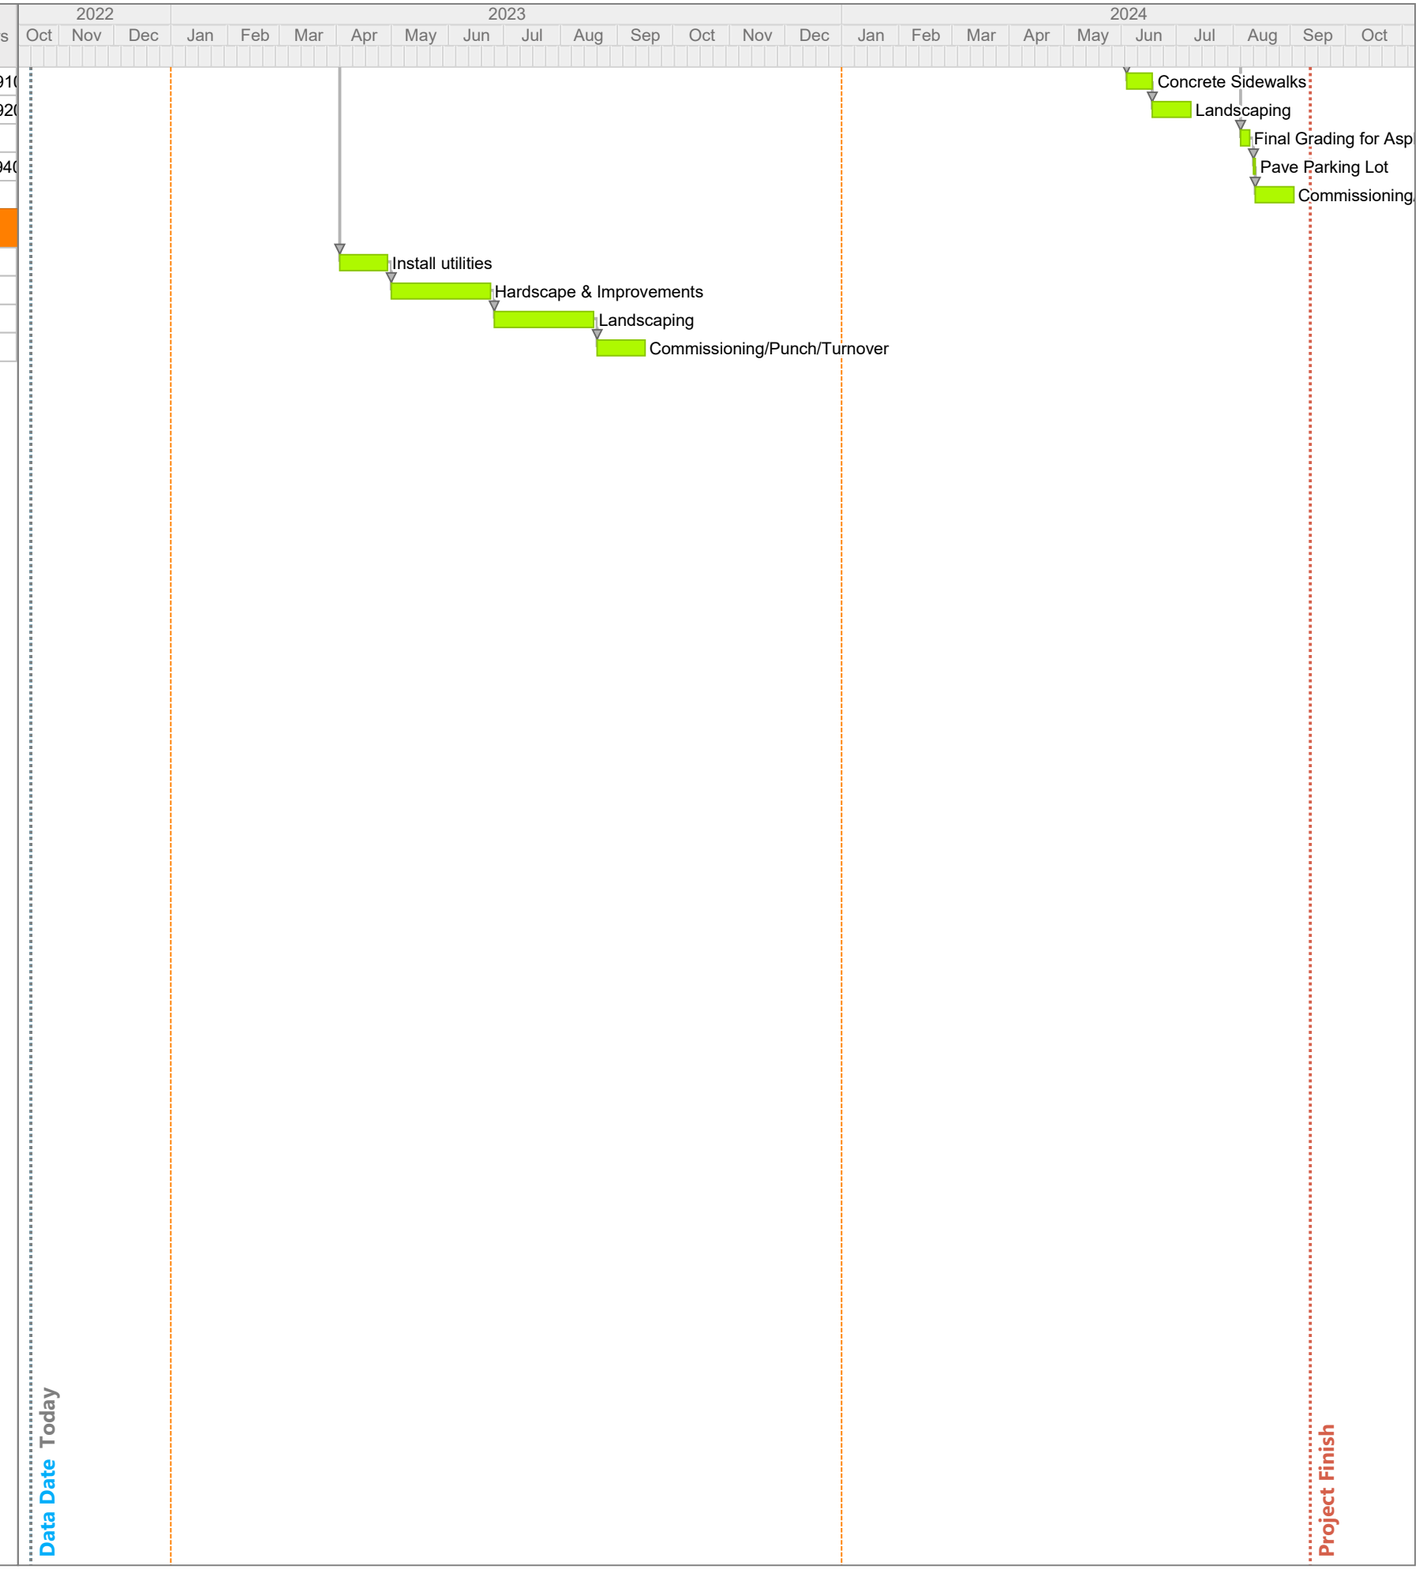
ID	Description	Original Duration	Start	Finish	Predecessors	Successors
5900	Concrete Sidewalks	10	06/04/24	06/17/24	5890FS*	5920FS, 5910
5910	Landscaping	15	06/18/24	07/08/24	5900FS*	5750FS, 5920
5920	Final Grading for Asphalt	5	08/05/24	08/09/24	5720FS, 5740	5930FS*
5930	Pave Parking Lot	1	08/12/24	08/12/24	5920FS*	5760FF, 5940
5940	Commissioning/Punch/Turnover	15	08/13/24	09/02/24	5930FS*	
Softball Field Improvements						
5950	Install utilities	20	04/03/23	04/28/23	5850FS*	5960FS*
5960	Hardscape & Improvements	40	05/01/23	06/23/23	5950FS*	5970FS*
5970	Landscaping	40	06/26/23	08/18/23	5960FS*	5980FS*
5980	Commissioning/Punch/Turnover	20	08/21/23	09/15/23	5970FS*
